Hilbers
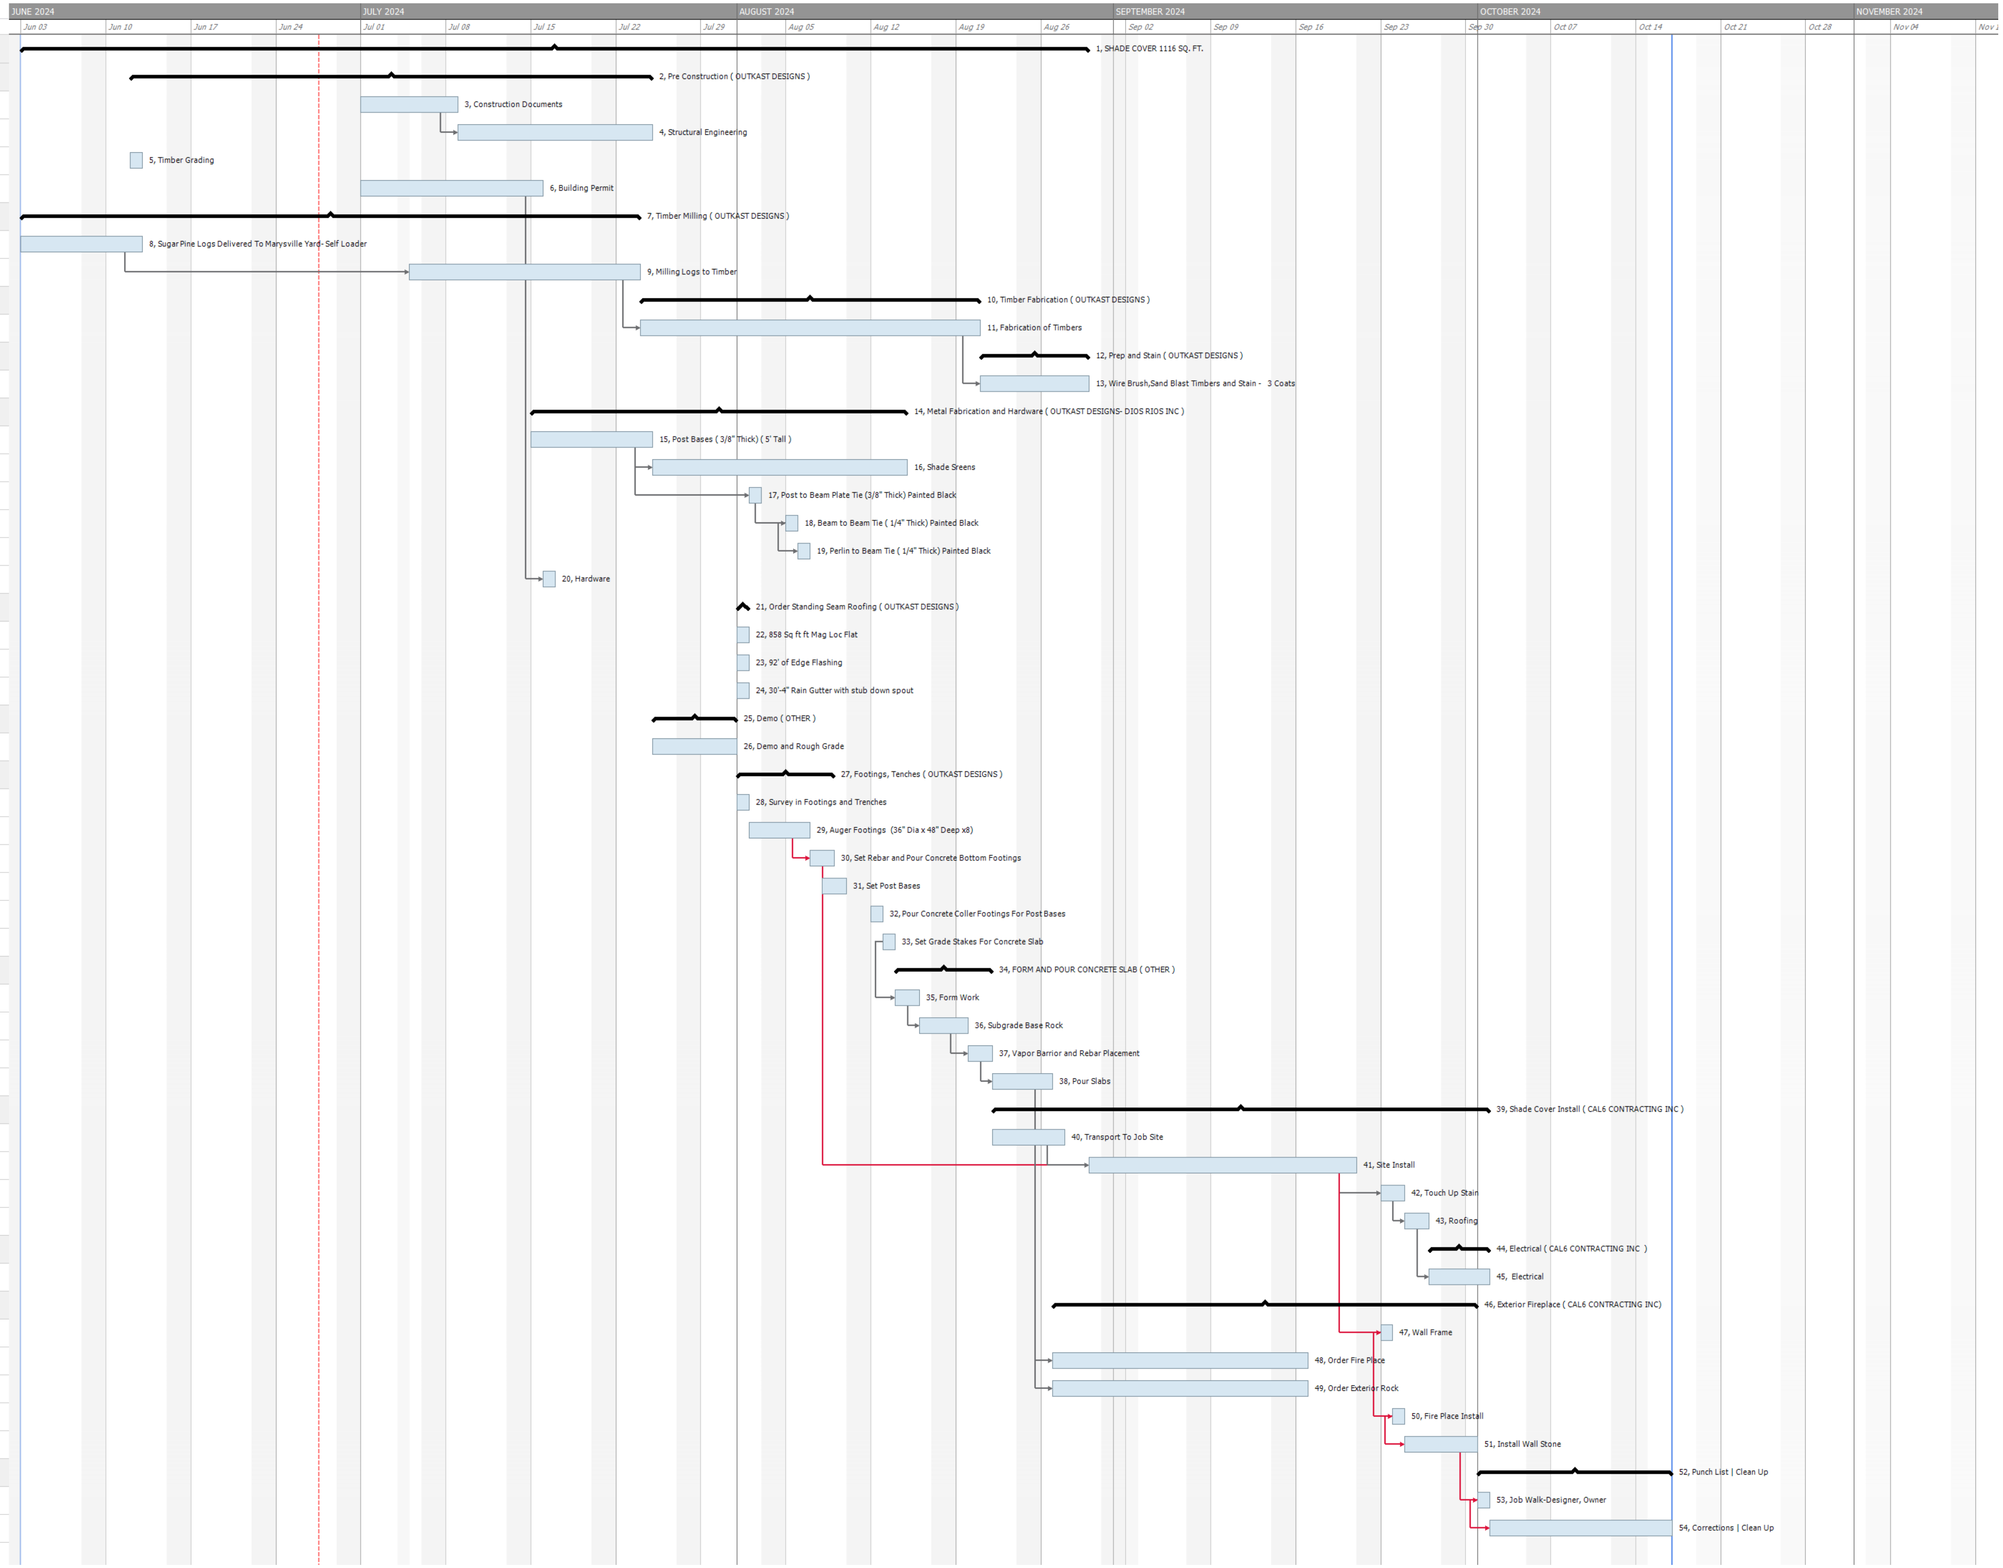
	NAME
1	**SHADE COVER 1116 SQ. FT.**
2	**Pre Construction (OUTKAST DESIGNS)**
3	Construction Documents
4	Structural Engineering
5	Timber Grading
6	Building Permit
7	**Timber Milling (OUTKAST DESIGNS)**
8	Sugar Pine Logs Delivered To Marysville Yard- Self Loader
9	Milling Logs to Timber
10	**Timber Fabrication (OUTKAST DESIGNS)**
11	Fabrication of Timbers
12	**Prep and Stain (OUTKAST DESIGNS)**
13	Wire Brush,Sand Blast Timbers and Stain - 3 Coats
14	**Metal Fabrication and Hardware (OUTKAST DESIGNS- DIOS RIOS INC)**
15	Post Bases (3/8" Thick) (5' Tall)
16	Shade Sreens
17	Post to Beam Plate Tie (3/8" Thick) Painted Black
18	Beam to Beam Tie (1/4" Thick) Painted Black
19	Perlin to Beam Tie (1/4" Thick) Painted Black
20	Hardware
21	**Order Standing Seam Roofing (OUTKAST DESIGNS)**
22	858 Sq ft ft Mag Loc Flat
23	92' of Edge Flashing
24	30'-4" Rain Gutter with stub down spout
25	**Demo (OTHER)**
26	Demo and Rough Grade
27	**Footings, Tenches (OUTKAST DESIGNS)**
28	Survey in Footings and Trenches
29	Auger Footings (36" Dia x 48" Deep x8)
30	Set Rebar and Pour Concrete Bottom Footings
31	Set Post Bases
32	Pour Concrete Coller Footings For Post Bases
33	Set Grade Stakes For Concrete Slab
34	**FORM AND POUR CONCRETE SLAB (OTHER)**
35	Form Work
36	Subgrade Base Rock
37	Vapor Barrior and Rebar Placement
38	Pour Slabs
39	**Shade Cover Install (CAL6 CONTRACTING INC)**
40	Transport To Job Site
41	Site Install
42	Touch Up Stain
43	Roofing
44	**Electrical (CAL6 CONTRACTING INC)**
45	Electrical
46	**Exterior Fireplace (CAL6 CONTRACTING INC)**
47	Wall Frame
48	Order Fire Place
49	Order Exterior Rock
50	Fire Place Install
51	Install Wall Stone
52	**Punch List | Clean Up**
53	Job Walk-Designer, Owner
54	Corrections | Clean Up
